

8TH ST SW PH 1 ROADWAY IMPROVEMENTS

PROJECT UPDATE


SEPTEMBER 17, 2020

Current Progress

Elder is working on removing the south two lanes of 8th Street.

Future Work

Starting on Tuesday September 22nd, there will be night work (7pm-7am) to remove and replace the intersection paving of 34th Ave SW and 8th St SW. This work will take at least two nights. During the night there will be no through traffic on 34th Ave SW, follow posted detour route. The intersection will be open to traffic during the day.

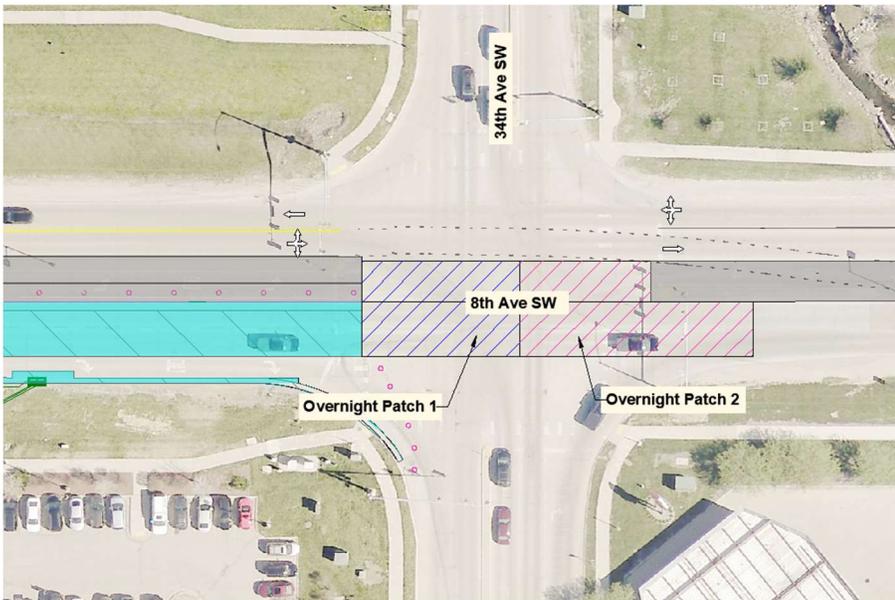

8th St SW and 34th Ave SW
Intersection Closure detail

Contractors will also begin construction of the new storm sewer that will be installed in the existing south ditch along 8th St SW.

Completion Date Stage 1 (between Hwy 65 to 34th Ave): Nov. 20, 2020

Final Completion Date: December 2021

Check the City Website for updates. Updates are posted to:
<http://www.altoona-iowa.com/departments/engineering-2/>

Or to receive updates via email, contact tmolitor@altoona-iowa.com

ALTOONA
NOW

IOWA DOT
SMARTER | SIMPLER | CUSTOMER DRIVEN

SNYDER
& ASSOCIATES

ELDER
CORPORATION

STERNQUIST
CONSTRUCTION

Contacts

City Engineer

John Dostart 515-957-5136
jdostart@altoona-iowa.com

Civil Engineer

Snyder & Associates
Ankeny, IA

8TH ST SW PH 1 ROADWAY IMPROVEMENTS

PROJECT UPDATE

SEPTEMBER 3, 2020


Current Progress

Work on the 8th St SW and 36th Ave SW intersection is on schedule and should be completed Saturday morning September 5th.

Traffic signal pole extensions will begin to be installed in the next few days. These will be used for when traffic runs head to head in the north two lanes.

Future Work

Starting on Tuesday September 8th, traffic will be switched to head to head traffic in the two north lanes of 8th Ave SW. This will allow for the work to begin in the south two lanes beginning with the concrete removal.

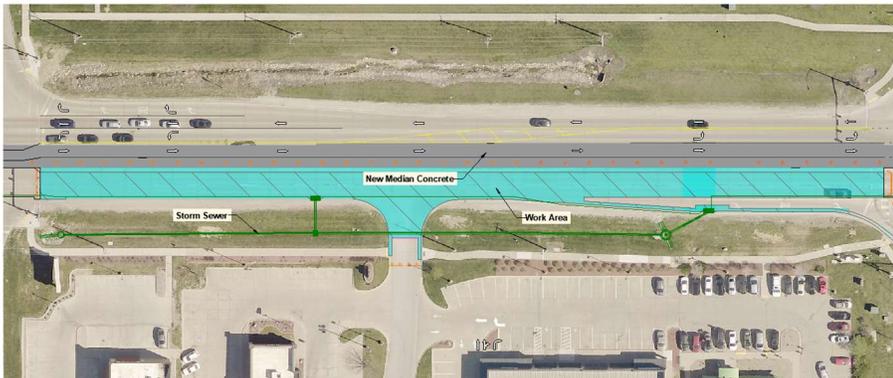

Section of 8th St SW
Showing Head to Head Traffic

Contractors will also begin construction of the new storm sewer that will be installed in the existing south ditch along 8th St SW.

In the next few weeks the intersection of 8th St SW and 34th Ave SW will have patch work similar to the 36th Ave intersection.

Completion Date Stage 1 (between Hwy 65 to 34th Ave): Nov. 20, 2020

Final Completion Date: December 2021

Check the City Website for updates. Updates are posted to:
<http://www.altoona-iowa.com/departments/engineering-2/>

Or to receive updates via email, contact tmolitor@altoona-iowa.com

ALTOONA
NOW

IOWA DOT
SMARTER | SIMPLER | CUSTOMER DRIVEN

S SNYDER
& ASSOCIATES

ELDER
CORPORATION

S STERNQUIST
CONSTRUCTION

Contacts

City Engineer

John Dostart 515-957-5136
jdostart@altoona-iowa.com

Civil Engineer

Snyder & Associates
Ankeny, IA

8TH ST SW PH 1 ROADWAY IMPROVEMENTS

PROJECT UPDATE

AUGUST 27, 2020


Current Progress

Over the past week Elder has been working on subgrade prep of the median turn lane. This required removing the dirt from the median and importing rock in to create a stable base for the pavement.

Starting on August 28th Sternquist will be paving the median turn lanes that have been removed. Weather pending median paving should be finished on Saturday, August 29th.

Future Work

Starting on Monday, August 31st, we will close the north and south bound lanes of traffic on 36th Ave SW crossing 8th St. There will also be no left turns off of 8th St on to 36th Ave. This will allow for the median lane to be completed in that intersection. This is scheduled for a 5 working day shutdown. It is anticipated for the intersection to reopen on Saturday, September 4th.

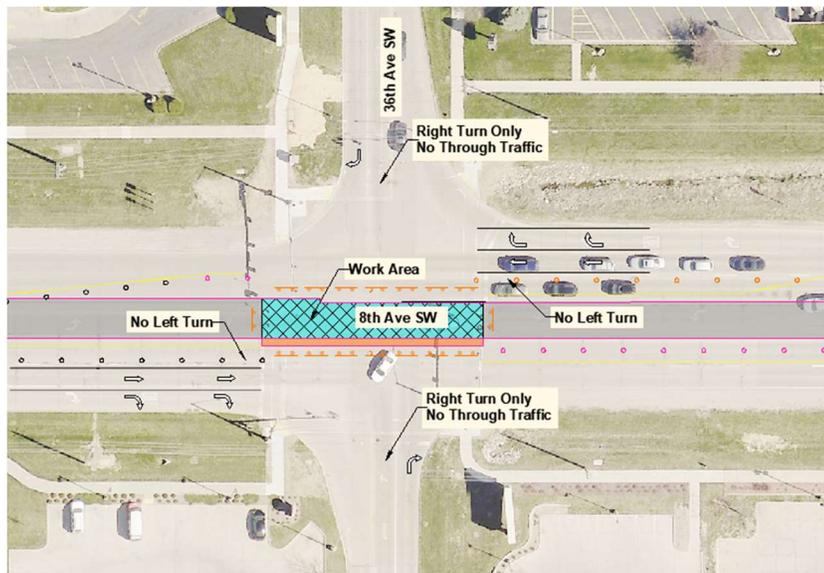

8th St SW 36th Ave SW
Intersection Closure Detail

Completion Date Stage 1 (between Hwy 65 to 34th Ave): Nov. 20, 2020

Final Completion Date: December 2021

Check the City Website for updates. Updates are posted to:
<http://www.altoona-iowa.com/departments/engineering-2/>

Or to receive updates via email, contact tmolitor@altoona-iowa.com

ALTOONA
NOW

IOWA DOT
SMARTER | SIMPLER | CUSTOMER DRIVEN

S
SNYDER
& ASSOCIATES

ELDER
CORPORATION

S
STERNQUIST
CONSTRUCTION

Contacts

City Engineer
John Dostart 515-957-5136
jdostart@altoona-iowa.com

Civil Engineer
Snyder & Associates
Ankeny, IA

8TH ST SW PH 1 ROADWAY IMPROVEMENTS

PROJECT UPDATE

AUGUST 20, 2020

Current Progress

On August 12th Elder Corporation began work on 8th Street SW. The first stage of construction involves removing the current median that separates the East and West bound lanes. The median will be paved as an additional traffic lane, so that it can be utilized for east bound traffic while reconstructing the East bound lanes.



8th St SW under the bypass
August 14, 2020

Future Work

Sternquist will be paving the median lane. Temporary signal extensions will be added to the mast arms of the traffic signals. This will allow the use of traffic signals for the head to head traffic during the reconstruction of the east bound lanes.

Elder will begin to install storm sewer and intakes in the existing ditch area. The intakes are needed due to the addition of curb and gutter on the East bound lanes of 8th St. Elder will also be connecting the box culvert located under 8th Street, near the intersection of 34th Ave SW, to the box culvert located under the Casey's driveway. This will allow for public sidewalk to be installed along 8th St SW.

Completion Date Stage 1 (between Hwy 65 to 34th Ave): Nov. 20, 2020

Final Completion Date: December 2021

Check the City Website for updates. Updates are posted to:
<http://www.altoona-iowa.com/departments/engineering-2/>

Or to receive updates via email, contact tmolitor@altoona-iowa.com

ALTOONA
NOW

IOWA DOT
SMARTER | SIMPLER | CUSTOMER DRIVEN

S
SNYDER
& ASSOCIATES

ELDER
CORPORATION

S
STERNQUIST
CONSTRUCTION

Contacts

City Engineer

John Dostart 515-957-5136
jdostart@altoona-iowa.com

Civil Engineer

Snyder & Associates
Ankeny, IA
